

Significant Factors in Agile Effort Estimation

by Pantjawati Sudarmaningtyas

Submission date: 06-Mar-2022 04:20PM (UTC+0700)

Submission ID: 1777492722

File name: Pantjawati_Rozlina_Manuscript_Rev_3.docx (1.03M)

Word count: 7402

Character count: 41117

SIGNIFICANT FACTORS ²⁷ IN AGILE EFFORT ESTIMATION

SIGNIFICANT FACTORS IN AGILE SOFTWARE DEVELOPMENT OF EFFORT ESTIMATION

Pantjawati Sudarmaningtyas^{1,2}, Rozlina Binti Mohamed^{1*}

¹Faculty of Computing, Universiti Malaysia Pahang, 26300 Gambang, Kuantan,
Pahang, Malaysia

²Department of Information System, Universitas Dinamika, 60298 Surabaya,
Jawa Timur, Indonesia

¹
pantja@dinamika.ac.id (Pantjawati Sudarmaningtyas), +62818399171
rozlina@ump.edu.my (Rozlina Binti Mohamed), +60199422871

*Corresponding Author

List of Table / Figure:

⁶
Table 1.

Table 2.

Table 3.

Table 4.

Table 5.

Table 6.

Table 7.

Table 8.

Table 9.

Figure 1.

Figure 2.

Figure 3.

Appendix 1.

Appendix 2.

SIGNIFICANT FACTORS IN AGILE SOFTWARE DEVELOPMENT OF EFFORT ESTIMATION

ABSTRACT

The Agile effort estimation involves project-related and people-related factors. This research objective is to find the factors that influence Agile effort estimation significantly through path analysis using a structural equation model. From theories and previous studies, this research built an agile effort estimation path coefficient model from six constructs. Project-related factors represent by requirement and design implementation constructs. People-related factors are measured by the construct of experience, knowledge, and technical ability. The last construct is the effort itself. This study employs SmartPLS for the confirmatory composite analysis and the structural model assessment. The confirmatory composite analysis shows that all constructs are reliable and valid. Furthermore, the structural model assessment found that all constructs in project-related factors have a positive relationship and significant influence indicated by coefficient path value of 59.1% between requirement and design implementation constructs. The same applies to all constructs representing people-related factors shown by coefficient path value of 67% between experience and knowledge, 42.6% between experience and technical ability, and 54.4% between knowledge and technical ability. In addition, all constructs proved influential simultaneously to effort by 31.1%. Positively contribute provided by requirement, experience, and technology's ability. While significantly influenced is provided by constructs of the developer's knowledge and technical ability. The largest effect is given by technical ability followed by knowledge and experience, despite in medium and small scale. Contrarily, the effects of project-related can be negligible because there was no influence from both constructs of their representatives. Based on the result, this study concludes that the significant

factors in Agile effort estimation are technical ability, knowledge, and experience.

Keywords: effort estimation, agile methodology, project-related factors, people-related factors, structural equation model, path analysis

INTRODUCTION

One of the crucial parts of a software project is effort estimation. The activity estimates the amount of effort necessary for developing the software product, in either man-days or man-hours. In addition, effort is a key factor that serves as a basis for calculating the cost and schedule needed for completing the project (Bloch et al., 2012). Generally, an effort is formed by a combination of people and time, which calculates from the number of productive working hours needed to complete a job. ²⁵ Man-hours, man-days, man-months, or man-years are typically used to express the units of effort (Trendowicz & Jeffery, 2014).

In contrast, agile software development methodology is more emphasis on coding, shorter delivery cycles, and several iterations to complete the software development. ~~Therefore, the effort estimation in this methodology is crucial because delivery time and project velocity are calculated based on the estimation results.~~ ²³ Another characteristic of Agile methodology is the collaborative and cooperative approach between all stakeholders, actively involving users and empowering the team to make decisions (Project-Management.com, 2019). The estimation process in Agile divides into two phases, namely, early estimation and iterative estimation. Early estimation was used to get the initial scope just enough to describe the entire software project. Meanwhile, iterative estimation conducted at the start of an iteration is to anticipate new or change requirements.

The top three methods currently used ¹ in agile are machine learning, expert judgment, and algorithmic. ~~The~~ Planning Poker technique is a part of the expert judgment method most implemented in Agile. Although this technique is in ² accordance with Agile characteristics, the result has shown bias value (Sudarmaningtyas & Mohamed, 2021). In addition, these methods heavily rely on the estimator experience and rarely involve other factors in the process of estimation.

The Agile estimation identified factors that are critical in determining software effort. In addition, people factors are also important because the estimation process involves a team of developers from different disciplines (Munialo & Muketha, 2016). Therefore, this study is conducted to find the significant factors that influence effort estimation in Agile.

Considering the importance of estimation efforts in Agile, expected the significant factors produced in this research can contribute to improving the existing Agile effort estimation method. In addition, implementation of those factors expected creates a better estimate of effort and increases accuracy while reducing the technicality and time required.

This paper organizes into five sections. Section 1 contains the research background, followed by describing related works. Section 3 discusses the research methodology that involves the path coefficient model development, questionnaire based on our research questions and hypothesis, examine and assess the structural model. Section 4 is the result and discussion of our findings, and the last section is wrapped up our conclusions.

RELATED WORKS

Agile software development (ASD) methods are lightweight methods that focus on simplicity, speed, self-organizing teams, and involving the customer as part of the team. Simplicity and speed can be achieved through more straightforward design and iterative development cycles. Each development cycle emphasizes delivering a demonstrable working product that focuses on the main functions. The customer involved in each development cycle is like a team member so that the requirement customer, who often changes, can be anticipated quickly by the team (Abrahamsson et al., 2002; Bourque & Fairley, 2014).

34
10 ASD is based on an iterative and incremental development model that promotes rapid response to changes and focuses on customer satisfaction, timely and continuous delivery, informal methods and minimal planning (Fernandez-Diego et al., 2020). ASD methods have several advantages, such as delivering working software faster, dealing with changing user requirements, and promoting better working relationships among all stakeholders (Zhang et al., 2010). Those advantages can significantly reduce the apparent overhead associated with heavyweight, plan-based methods used in large-scale software development projects and resolve issues of slow execution on concurrent engineering (Boehm, 2006; Bourque & Fairley, 2014).

18
5 Scrum, Xtreme Programming (XP), Test Driven Development (TDD), Agile Unified Process (AUP), Kanban, and Distributed Agile Software Development (DASD) are ASD dynamic methods available for developing a software product. Each method has its unique attributes and qualities, so choosing the proper method is a critical task, and it should be based on the project requirements (Fernandez-Diego et al., 2020; Prakash & Viswanathan, 2017).

Effort estimation is a crucial part of ASD for three reasons: 1) maximize project velocity; 2) optimize individual developer effort across multiple projects; 3) optimal scheduling to achieve global efficiencies (Malgonde & Chari, 2018). The majority of the effort estimation method used in ASD is the expert judgment method, especially the Planning Poker technique (Sudarmaningtyas & Mohamed, 2021).

2 Following the characteristics of ASD, effort estimation is usually conducted by structured group consensus and lightweight approaches. In addition, it is also based on the user story that delivers in one or two sentences contains pieces of functionality or feature software worth for the user. (Trendowicz & Jeffery, 2014). Commonly, estimates conducted periodically, internally

generated, and must be involved stakeholders to compromise, review, and reach an agreement concerning the number of resources and time to finish the projects (Bourque & Fairley, 2014). Provide an approximation of the resources needed to complete a project, especially delivery products or services in accordance with the specified characteristics of functional and non-functional is the objective of estimation effort (Project Management Institute, 2017).

Instead of giving by a single value, the estimation value is better expressed in intervals because estimator confidence that of a possibility that the actual efforts will be within range (Jørgensen, 2016). In addition, it could also provide three estimates: best-case (optimistic), normal-case (most likely), and worst-case (pessimistic) scenarios. To obtain best-case and worst-case scenarios, multiply percentages according to the organization's norms and confidence level in the opportunity in question with normal-case (Chemuturi, 2009).

The Agile effort estimation is influenced by factors related to the project and factors related to people. The factors related to the project include the type of project, quality requirements, hardware and software requirements, ease of operation, complexity, data transaction, and multiple sites. People-related factors consist of communication skills, familiarity in a team, managerial Skills, security, working time, the experience of the previous project, and technical ability (Popli & Chauhan, 2014). Accuracy in the agile effort estimation relied heavily on the expertise of professionals in software development. Thereby that estimation conducts by expert groups could be diminished the optimism bias arising from group discussion (Lenarduzzi et al., 2015; López-Martínez et al., 2018; Mahnič & Hovelja, 2012).

METHODOLOGY

Development of Path Coefficient Model

In the Agile effort estimation, the project factors are essential to determine. In addition, people factors are also important because the estimation process involves a team of developers from different disciplines (Munialo & Muketha, 2016; Popli & Chauhan, 2014). People-related factors represented the expertise of each team showed by the experience, domain knowledge, and technical ability (Popli & Chauhan, 2014). To get better results, estimation effort should include observance of various factors derived from software development methodology. For that reason, project-related factors acquired from an Agile development methodology consist of two activities which are: requirement engineering, and design implementation (Chemuturi, 2009; Sommerville, 2011). The mapping factors are based on the theoretical aspect of the previous research described in Table 1.

Table 1
Mapping factors based on the theoretical aspect

People factors	Agile Development Methodology	
	Requirement Engineering	Design Implementation
Experience	The quality requirements	Ease of operation
Domain knowledge		Complexity
Technical ability		Data transaction

This study constructs a relation of factors grounded in previous literature studies, and the graph consists of three parts, as depicted in Figure 1. The first part, indicated with the orange dash line, represents project-related factors derived from the Agile development methodology column in Table 1, comprising two variables. The second part, the area surrounded by the blue dash line, corresponds with the people factors column, containing three variables. Finally, the last part reflects the effort itself. Survey results will confirm the relation of factors in this graph to achieve this research objective.

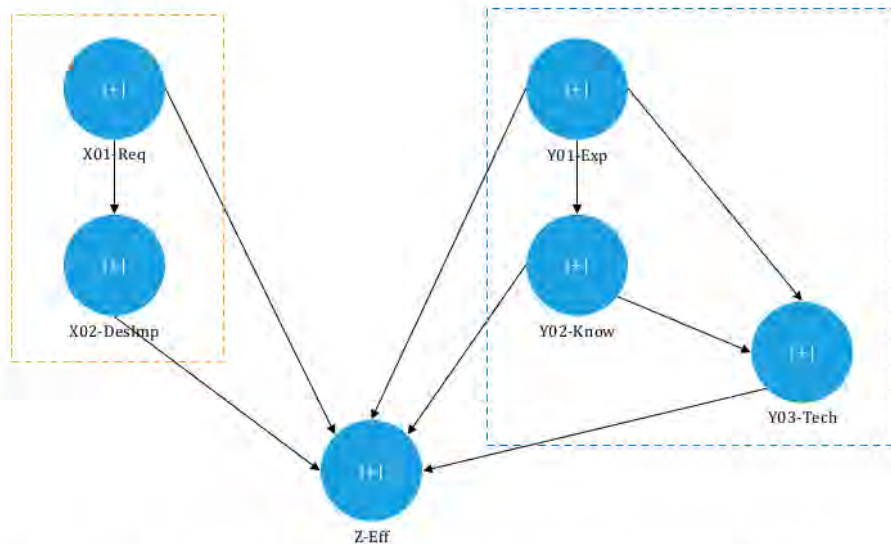


Figure 1. The Factors Relation Grounded in Previous Literature Studies

Project-related factors comprise of requirement variable, and design implementation variable; that symbolized by X01-Req and X02-DesImp respectively. People-related factors; indicated by Y01-Exp, Y02-Know, and Y03-Tech are represented by experience, knowledge domain, and technical ability. In addition, the effort constructed is denoted by Z-Eff. Based on theory, variable in the project-related factors has correlation, where the requirement influences design implementation. On the other hand, variable in the people-related factors has a relation that assumes that developer's experience would leverage their knowledge and technical ability. In addition, technical ability is also affected by knowledge. Therefore, the requirement, design implementation, experience, knowledge, and technical ability influence the effort.

This study proves assumptions on this model through nine (9) hypotheses constructed based upon research questions emerge. Table 2 reveals the research questions derived from this model and the hypotheses related to the research

questions. The first column contains research questions about the relationship of any constructs, while the next column explains hypotheses related to those research questions.

Table 2
Research question lead hypotheses

Research Question	Hypothesis
RQ1: Do requirements influence the design implementation?	H1: The Requirement construct is positively related to the design implementation construct.
RQ2: Do requirements affect effort estimation?	H2: The Requirement construct is positively related to the effort construct.
RQ3: Do design implementation affect the effort?	H3: The construct of design implementation is positively related to the effort construct.
RQ4: Does experience have an impact on a developer's knowledge domain?	H4: The experience construct is positively related to the knowledge domain construct.
RQ5: Does experience influence a developer's technical ability?	H5: The experience construct is positively related to the technical ability construct.
RQ6: Do experience influence effort estimation?	H6: The experience construct is positively related to the effort construct.
RQ7: Does the knowledge affect the developer's technical ability?	H7: The knowledge domain construct has positive relationships with the technical ability construct.
RQ8: Does knowledge have an impact on effort estimation?	H8: The knowledge domain construct has positive relationships with the effort construct.
RQ9: Does the technical ability influence effort estimation?	H9: The construct of technical ability has a positive relationship with effort.

The relationship and influence between constructs are captured in Table 3. The relation notation between two constructs is written in the first column, relation direction in the second column, and the associated hypotheses number in the last column.

Table 3
Structural relationships and hypotheses

Structural Relationships	Direction	Hypothesis
X01-Req -> X02-DesImp	+	H1
X01-Req -> Z-Eff	+	H2
X02-DesImp -> Z-Eff	+	H3

Table 3
Structural relationships and hypotheses

Structural Relationships	Direction	Hypothesis
Y01-Ex -> Y02-Know	+	H4
Y01-Ex -> Y03-Tech	+	H5
Y01-Ex -> Z-Eff	+	H6
Y02-Know -> Y03-Tech	+	H7
Y02-Know -> Z-Eff	+	H8
Y03-Tech -> Z-Eff	+	H9

The first column in Table 3 contains a notation of relations between two constructs, and the second column contains the relation direction. For example, the structural relationship denoted X01-Req -> X02-DesImp indicates that the requirement construct influences the design implementation construct. When X01-Req positively influences X02-DesImp, the direction column fills by a plus sign (+). In contrast, the negative direction relationship signaled the negative impact between the two constructs.

Questionnaire

To confirm the relations of those factors conducted by the survey through distributed questionnaire was developed based on six constructs in Figure 1, and several indicators measure each construct. The association between factor, construct, and indicator is revealed in Table 4.

Table 4
Factor, construct, and indicator relationship

Factor	Derived from Previous Literature Studies	Construct	Indicator	Description
Requirement Engineering Design Implementation	Requirement	Requirement	Functional requirement Non-functional requirement	Measure the quality requirements
	Design	Design	User interface	Assess the ease of operation
	Implementation	Implementation	Software and hardware interfaces Diversity of technology The sophisticated or novelty technology	Represent the complexity

Table 4
Factor, construct, and indicator relationship

Factor from Literature Studies	Derived Previous	Construct	Indicator	Description
Experience		Experience	Coding Complexity Database Size Database Complexity Job experience Effort estimation experience	Element of the data transaction Indicators are used to measure the estimator experience
Domain Knowledge		Domain Knowledge	Similar project Good track record	Estimator domain knowledge assessed by the frequency of involvement in the similar project and its track records
Technical Ability		Technical Ability	Technical ability Involve in many projects	Technical ability is evaluated by the level estimator technical ability and the number of projects involved.
Effort		Effort	Guess/intuition Experience Track record Attributes	The way of estimating effort

Construct is a representative of a conceptual definition built from a set of indicators. An indicator is in the form of a single variable used in conjunction with one or more variables to form a composite measure, where each indicator has attributes. Attributes embedded in indicators are complexity and size because these attributes mostly used agile effort estimation in the last three years (Fernandez-Diego et al., 2020; Sudarmaningtyas & Mohamed, 2021). All constructs, indicators, and attributes used in the questionnaire are briefly described in Table 5, and the questionnaire that used to collect data entirely served in Appendix 1.

Table 5
Questionnaire constructs and indicators

Construct	Scales Type	Indicator	Description	
X01-Req (Requirement)	1: Never (0%)	X1: Functional requirement Complexity	Frequency of the complexity of <i>functional requirement</i> considered by developers in estimating efforts.	
	2: Occasionally (30%)	X2: Non-functional requirement Complexity	Frequency of the complexity of <i>non-functional requirements</i> considered by developers in estimating efforts.	
X02-DesImp (Design Implementation)	3: Sometimes (50%)	X3: User interface Complexity	In effort estimation, directly or indirectly, consider the complexity of software user interface	
	4: Normally (80%)	X4: Software and hardware interfaces Complexity	In effort estimation, directly or indirectly, consider the complexity of interfaces between software and hardware	
	5: Always (100%)	X5: Diversity of technology	In effort estimation, directly or indirectly, consider the diversity technology that uses	
		X6: The sophisticated or novelty technology	In effort estimation, directly or indirectly, consider the sophisticated or novelty technology that uses	
		X7: Coding Complexity	In effort estimation, directly or indirectly, consider the difficulty level of coding	
		X8: Database Size	In effort estimation, directly or indirectly, consider the database size	
		X9: Database Complexity	In effort estimation, directly or indirectly, consider the database complexity	
	Y01-Exp (Experience)	12 1: None;	Y1: Job experience	Adequate job experience can affect a person to produce more accurate estimates
		2: Low;	Y2: Effort estimation experience	Experience in estimating effort may affect one individual to produce a more accurate estimate.
Y02-Know (Domain Knowledge)	3: Fair;	Y3: Similar project	Frequently involved in similar projects can affect a person to produce more accurate estimates.	

Table 5
Questionnaire constructs and indicators

Construct	Scales Type	Indicator	Description
Y03-Tech (Technical Ability)	4: High; 5: Very High.	Y4: Good track record	A good track record in previous projects can affect a person to produce more accurate estimates.
		Y5: Technical ability	Developers who have technical expertise can produce more precise estimates.
		Y6: Involve in many projects	Involving in many projects can affect a person to produce more accurate estimates.
Z-Eff (Effort)	0: No; 1: Yes.	Z1: Guess/intuition	Mechanism of estimating effort just by guessing or based on intuition.
		Z2: Experience	Mechanism of estimating effort based on experience.
		Z3: Track record	Mechanism of estimating effort based on previous projects track record.
		Z4: Attributes	Mechanism of estimating effort using specific attributes that are related to the project.

19 Requirement constructs have two indicators because software system requirements are generally classified as functional requirements or non-functional requirements. The indicators are used to measure design implementation, classified by the interface, technology, developing programs, and database. The chosen indicator represents an important design implementation process because most of the agile methods users did not require detailed design documentation. Interface indicator denoted by the user interface and hardware-software interface. Technology is represented by indicators of diversity and sophistication or novelty. Finally, coding is an indicator for developing a program, while the size and complexity indicators represent the (Hamouda, 2014; Khatri et al., 2016; Pasuksmit et al., 2021; Rosa et al., 2021; Sommerville, 2011; Yuliansyah et al., 2018).

The developer's experience, domain knowledge about the project, and technical ability are important aspects of software project development

experience measured by job experience and effort estimation experience. In addition, domain knowledge is measured by being frequently involved in similar projects and has a good track record in previous projects. Finally, technical ability is measured by the developer's technical ability and involvement in many projects (Adnan & Afzal, 2017; Fernandez-Diego et al., 2020; Popli & Chauhan, 2014).

How to perform the effort estimation be an indicator of effort. Perform effort estimation through guess or intuition is the first indicator. The second indicator performs ²² effort estimation based on experience. The third estimation effort is based on the track record in previous projects, and the last is using attributes-related projects to estimate the effort (Popli & Chauhan, 2013).

Respondents

Agile effort estimation is usually done through a group discussion that has an advantage empowered developers' team to decide the estimated effort (Sudarmaningtyas & Mohamed, 2020). Therefore, this study is targeting developers as respondents. In addition, ¹ estimation efforts conducted by the developers have higher accuracy than ¹ beginner's estimates (Lenarduzzi et al., 2015; López-Martínez et al., 2018, 2017). ¹ The expertise of professionals in software development is the primary aspect that influences estimation accuracy through Planning Poker. The estimation conducts by expert groups could be diminished ¹ the optimism bias arising from group discussion (Lenarduzzi et al., 2015; López-Martínez et al., 2018; Mahnič & Hovelja, 2012).

The sample size was determined by G*Power software because the previous studies did not specifically mention the number of respondents. Our sample size is calculated with criteria t-test linear multiple regression with significant error 5%, effect size 0.35, and 5 predictors. With those criteria, the minimal sample size that G*Power suggests is 40. The source data in this study were collected from 41 developers as respondents, which is the fulfilment of the

minimal sample size. Respondent demographics are classified by gender and three aspects, as revealed in Table 6.

Table 6
Respondent demographics

Aspect	20	Male	Female	Total
Job Experience	> 10 years	5	3	8
	6 – 10 years	6	1	7
	3 – 5 years	10	4	14
	< 3 years	12	0	12
	Total	33	8	41
Project Experience	> 10 projects	16	4	20
	6 – 10 projects	7	0	7
	3 – 5 projects	7	3	10
	< 3 projects	3	1	4
	Total	33	8	41
Conduct Effort Estimation	Always (100%)	11	3	14
	Normally (80%)	17	3	20
	Sometimes (50%)	5	2	7
	Occasionally (30%)	0	0	0
	Never (0%)	0	0	0
Total	33	8	41	

The above table shows that respondents dominated by males are as much as 80%, while 20% is female. In addition, 71% of respondents have job experience of more than three years and 66% have been involved in more than six projects. Most respondents (83%) have experience in effort estimation, and 95% of respondents believe that effort estimation result is more accurate when attributes associated with the project are considered during estimation. Raw data obtained from the survey contained in Appendix 2.

Examine And Confirm the Structural Model

The structural model examined and confirmed through executing a confirmatory composite analysis (CCA) with evaluating path coefficients, construct reliability, and construct validity. Path Coefficients are measured by the indicator loadings. Construct Reliability can be assessed using two approaches: the traditional approach of Cronbach's alpha, and composite reliability. However, composite

reliability is the preferred reliability metric for structural equation modelling (SEM) statistical techniques. Construct Validity is evaluated by examining convergent and discriminant validity (Hair.Jr. et al., 2020).

The path coefficient examined by the values of indicator loadings should be at least 0.50 and ideally 0.708 or higher. The reliability of constructs is suggested to be above 0.70 for both Cronbach's alpha and composite reliability. Convergent validity is measured by the average variance extracted (AVE) with a value of at least 0.5. Discriminant validity is evidenced when a reflective construct has the strongest relationships with its own indicators compare with any other construct in the path model. Discriminant validity is evaluated through the result of the Fornell-Larcker criterion. On this criterion, the shared variance within the constructs should be larger than the shared variance between the constructs (Bourque & Fairley, 2014).

Assess The Structural Model

The structural model, as known as the inner model, was assessed by evaluating the size and significance of the structural path relationships, assess R^2 , examine the f^2 effect size, and evaluate the predictive relevance based on Q^2 . Evaluating the size and significance of the structural path relationships is required to examine whether the determined hypotheses gain empirical support that indicated by t values exceed +/- 1.645. The goal of assess R^2 is to measure the variance of endogenous variables exhibited X02-DesImp, Y02-Know, Y03-Tech, and Z-Eff (Hair.Jr. et al., 2020).

The f^2 statistics indicate the relative strength of each independent variable in predicting the dependent variable. The f^2 was evaluated by observing the change in R^2 when each independent variable was excluded in turn. The f^2 value of 0.02, 0.15 and 0.35 represents small, medium, and large effects (Hair.Jr. et al., 2020).

$$f^2 = \frac{R_{included}^2 - R_{excluded}^2}{1 - R_{included}^2} \quad (1)$$

Predictive accuracy by evaluating the Q^2 where the positive value indicates that the developed model can accurately predict data points reflective indicators of endogenous variables (Hair.Jr. et al., 2020).

RESULTS AND DISCUSSION

Confirmatory Composite Analysis

The preliminary path coefficient model to find significant factors in Agile effort estimation (AEE) has six constructs and 19 indicators, as revealed in Figure 2. Two constructs in project-related factors measured by 11 indicators where requirement constructs have two indicators, while the design implementation construct are supported by nine indicators. Each construction represents a people-related factor measured by two indicators, and the rest contributes to the efforts' construct. We implement the preliminary path coefficient model in SmartPLS.

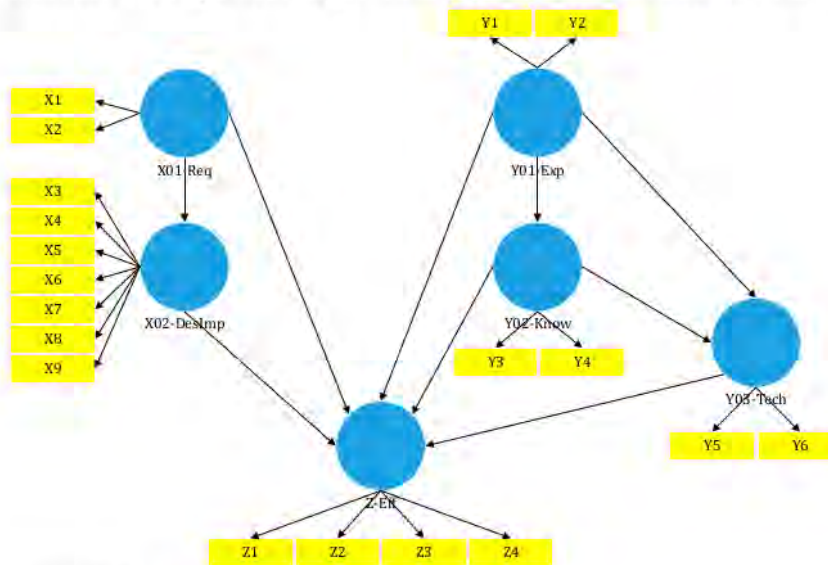


Figure 2. Preliminary Path Coefficient Model

The result of outer loading in the first running found that indicators X7 and Z1 in X02-DesImp and Z-Eff constructs have insignificant *t* Statistic. Consequently, those indicators were omitted from the preliminary model. In the second executing, the X02-DesImp construct AVE value is lower than requisite. Therefore, X8 as the indicator with the lowest outer loading is deleted. Thus, the X02-DesImp construct is expected to reach the value of the required AVE. Finally, all constructs have achieved the requisite AVE value in the third running, and the confirmed path coefficient model is depicted in

Figure 3.

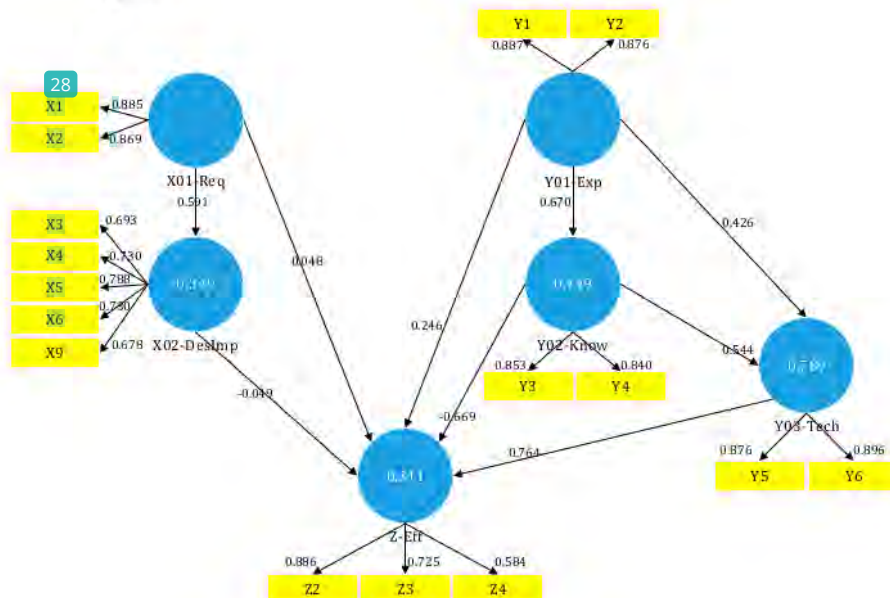


Figure 3. Confirmed Path Coefficient Model

In the confirmed path coefficient model, almost all indicators have ideal factor loadings values, except X3, X9, and Z4. Although the factors are not ideal, the third indicator complied with the rule as the load factor value is above 0.5.

The third indicator has fulfilled the rule because the loading factor value is above 0.5.

Constructs that represent project-related factors, both indicators in the constructs of Requirement (X01-Req) can be measured significantly with the loadings of functional requirement (X1) is 88.5%, and non-functional requirement (X2) is 86.9%. In addition, construct of Design and Implementation (X02-DesImp) influenced significantly worth 69.3% of the user-interface complexity (X3), 73% of the complexity of the software-hardware interface (X4), 78.8% by a variety of technologies (X5), 73% of sophisticated/novelty of the technology (X6), and 67.8% of complexity database (X9). However, the Design and Implementation constructs are insignificantly influenced by indicators of difficulty of coding (X7) and database size (X8).

In contrast to project-related factors, all indicators on each construct representing the people-related factors can significantly influence because they have loadings factor values above the ideal value. In addition, the construct of Effort (Z-Eff) has the same situation as the X02-DesImp construct, where not all indicators are influential significantly. The indicators that significantly influence Z-Eff are Z2, Z3, and Z4 with loadings factor values worth 88.6%, 72.5%, and 58.4%, while indicator Z1 (guessing/intuition) proved no effect.

A conventional reliability assessment with Cronbach's alpha indicates that four constructs have good reliability, while the others are classified as acceptable. Likewise, composite reliability, the preferred reliability metric in SEM, reflects good reliability because the value is above 0.70 for all constructs. Therefore, all constructs in this model are reliable and valid, as shown in Table 7.

Convergent validity assessed by AVE demonstrates good validity because the AVE value is above 0.5 for all constructs. In addition, discriminant validity assessed by Fornell-Larcker also indicates good validity. It is supported the value

of the reflective construct with its own indicators are higher than any other construct in the path model.

Table 7
Results of reliability assessment

26 Construct	Reliability Assessment		Validity Assessment	
	<i>Cronbach's Alpha</i>	<i>Composite Reliability</i>	<i>AVE</i>	<i>Fornell-Larcker</i>
X01-Req	0.700**	0.869**	0.769	0.877***
X02-DesImp	0.776**	0.847**	0.525	0.725***
Y01-Exp	0.713**	0.874**	0.777	0.881***
Y02-Know	0.604*	0.835**	0.716	0.846***
Y03-Tech	0.726**	0.879**	0.784	0.886***
Z-Eff	0.576*	0.781**	0.550	0.742***

Note:

*Acceptable; **Good; ***The value of the reflective construct with its own indicators are higher than any other construct.

Measurement quality of the CCA result shows that all constructs in the path coefficient model can be confirmed. This result is also assured that the six reflectively measured composite constructs in the confirmed path coefficient model are reliable and valid.

The Structural Model Assessment

Estimates of path coefficients and significance of the structural path relationships is conducted to examine whether there is empirical support for the pre-determined hypotheses. Five hypotheses (H1, H4, H5, H7, H9) are empirically supported because they have consistent and significant values with hypothesized ones. Although H2 and H6 have a positive direction but are insignificant; in contrast, H8 has a significant influence although a negative tendency. In addition, H3 has inconsistent signs and is insignificant. Path coefficients and significance testing as the result of SmartPLS revealed in Figure 3 are presented in Table 8.

The path coefficient values, and *t* Statistic indicate that the Requirement construct is positively related and significantly influences the Design and implementation construct. Thereby, the H1 hypothesis is accepted. Thus, an increase of 55.9% on the construct of Design and implementation for each increase occurred in the Requirement construct. On the other hand, the Requirement construct is positively related to the Effort construct, although the influence is insignificant. It means the H2 hypothesis is also acceptable.

Table 8
Path coefficients and significance testing

Hypothesis	Structural Relationships	Path Coefficients	<i>t</i> Statistic
H1	X01-Req -> X02-DesImp	0.591	4.912**
H2	X01-Req -> Z-Eff	0.048	0.184
H3	X02-DesImp -> Z-Eff	-0.049	0.203
H4	Y01-Exp -> Y02-Know	0.670	4.926**
H5	Y01-Exp -> Y03-Tech	0.426	3.686**
H6	Y01-Exp -> Z-Eff	0.246	0.774
H7	Y02-Know -> Y03-Tech	0.544	5.034**
H8	Y02-Know -> Z-Eff	-0.669	2.173*
309	Y03-Tech -> Z-Eff	0.764	2.511*

Note: * $p < 0.05$; ** $p < 0.01$

Design and Implementation construct not positively related and influences insignificant to Effort construct. In other words, every increase in Design and Implementation construct will decrease the Effort construct by 4.8%. Due to that reason, the H3 hypothesis is rejected.

The Experience construct has positively related to the constructs of Knowledge, Technical Ability, and Effort. This construct significantly influences the Knowledge construct as 67%, while the Technical Ability construct is influenced by 42.6%. Nevertheless, this construct is insignificant on the Effort construct. Therefore, based on the statement, the hypotheses of H4, H5, and H6 are acceptable.

Knowledge constructs significantly influence the technical ability and Effort constructs, respectively, reaching 54.4% and 66.9%. However, the

Knowledge construct contrasts with the other constructs because it has negatively related to the Effort construct. Therefore, hypothesis H7 is acceptable nevertheless rejects hypothesis H8.

Hypothesis H9 is acceptable because the Technical Ability construct has positively associated and significantly influence the Effort construct. Every improvement in the Technical Ability constructs increases the Effort construct by 76.4%.

Observing R^2 values shows the ability of exogenous constructs in clarifying endogenous constructs. The exogenous construct X01-Req gives moderate influences by 34.9% to endogenous construct X02-DesImp, while exogenous construct Y01-Exp gives strong influences as 44.9% to endogenous construct Y02-Know. Endogenous variable Y03-Tech got strong influence simultaneously from exogenous constructs Y01-Exp and endogenous construct Y02-Know as 78.9%. The last endogenous construct is Z-Eff that simultaneously influenced by constructs X01-Req, X02-DesImp, Y01-Exp, Y02-Know, and Y03-Tech by 31.1%. This indicates that the Effort construct was also influenced by another construct not mentioned in this study.

The interest of this study is on the effect size of endogenous construct Z-Eff. Construct Y01-Exp contributes a small size effect to Z-Eff by 0.028. On the other hand, the constructs of Y02-Know and Y03-Tech give a medium effect size to the Z-Eff. In addition, the effect of X01-Req and X02-DesImp is considered negligible because it did not affect the Z-Eff construct. Constructs that account for most of the variance in Z-Eff is Y03-Tech followed by Y02-Know with effect size f^2 is 0.164 and 0.155. The results of examining the f^2 effect size are completely served in Table 9.

The evaluation revealed that all endogenous constructs have Q^2 values: X02-DesImp of 0.148, Y02-Know has 0.279, Y03-Tech by 0.576, and Z-Eff is

worth 0.102. This evaluation indicated all Q^2 values are above 0.0, which means the confirmed path coefficient model able to provide relevant predicting for all endogenous constructs.

Table 9
Examine the f^2 effect size

	R^2 for Z-Eff	f^2 Effect Size
R2 Includes all variable	0.311	
R2 Excludes X01-Req	0.309	0.003
R2 Excludes X02-DesImp	0.310	0.001
R2 Excludes Y01-Exp	0.292	0.028
R2 Excludes Y02-Know	0.204	0.155
R2 Excludes Y03-Tech	0.198	0.164

CONCLUSION

This study found that the project-related factors, represented by requirement and design implementation, and people-related factors, consist of experience, knowledge, and technical ability, proved influential simultaneously to effort by 31.1%. This outcome supports and aligns with Popli and Chauhan's (2014) research result and Munialo and Muketha's (2016). Although all factors simultaneously influence effort, not all the factors that have a positive relationship and significant influence. According to our acceptable hypotheses, requirement, experience, and technology's ability positively contribute to Agile effort estimation. In addition, Agile effort estimation is significantly influenced by the developer's knowledge and technical ability.

The assessment on the people-related factors provides effect size to effort on a small scale and medium scale where technical ability (Y03-Tech) gives the largest effect size followed by knowledge (Y02-know) and experience (Y03-Exp). Contrarily, the effects of project-related can be negligible because there was no influence from both constructs of their representatives. This is consistent with the previous results, stating that requirement, and designs & implementation do not significantly influence the effort. Therefore, this study concludes that people-

related factors, especially technical ability, knowledge, and experience, are significant in Agile effort estimation.

Our conclusion is supported by the research finding of Asnawi et al. (2012) that software developers' involvement is the top factor in Agile methods. In addition, our acceptable hypotheses strengthened the conclusions research of Ramessur & Nagowah (2020) that stated the two most impacting factors in Agile projects are staff experience and technical ability, and complexity of requirements.

Further research is built more accurate Agile effort estimation by implementing those significant factors. In addition, exploring the other factors that influence agile effort estimation is also important because, based on our findings, the simultaneous influence on project-related and people-related factors is 31.1%. This value convinces that there are still many other indicators that future researchers can explore.

ACKNOWLEDGMENT

The work is supported in part by UMP-UIAM-UITM under Grant Nos. RDU200755 with title “Design and Event Management Prioritization Framework Exploiting Fuzzy Ahp and Fuzzy Topsis Approaches”.

REFERENCES

- Abrahamsson, P., Salo, O., Ronkainen, J., & Warsta, J. (2002). Agile Software Development Methods: Review and Analysis. In *VTT Publication 478*. TT Publication 478. <http://arxiv.org/abs/1709.08439>
- Adnan, M., & Afzal, M. (2017). Ontology Based Multiagent Effort Estimation System for Scrum Agile Method. *IEEE Access*, 5, 25993–26005. <https://doi.org/10.1109/ACCESS.2017.2771257>
- Asnawi, A. L., Gravell, A. M., & Wills, G. B. (2012). Factor Analysis: Investigating Important Aspects for Agile Adoption in Malaysia. *2012 Agile*

India, 60–63. <https://doi.org/10.1109/AgileIndia.2012.13>

- Bloch, M., Blumberg, S., & Laartz, J. (2012). *Delivering Large Scale IT.pdf*. <https://www.mckinsey.com/business-functions/digital-mckinsey/our-insights/delivering-large-scale-it-projects-on-time-on-budget-and-on-value>
- Boehm, B. (2006). A view of 20th and 21st century software engineering. *Proceeding of the 28th International Conference on Software Engineering - ICSE '06*, 12–29. <https://doi.org/10.1145/1134285.1134288>
- Bourque, P., & Fairley, R. E. (2014). *Guide to the Software Engineering - Body of Knowledge*. IEEE Computer Society. <https://doi.org/10.1234/12345678>
- Chemuturi, M. (2009). *Software Estimation Best Practices, Tools & Techniques: A Complete Guide for Software Project Estimators*. J. Ross Publishing.
- Fernandez-Diego, M., Mendez, E. R., Gonzalez-Ladron-De-Guevara, F., Abrahao, S., & Insfran, E. (2020). An Update on Effort Estimation in Agile Software Development: A Systematic Literature Review. *IEEE Access*, 8, 166768–166800. <https://doi.org/10.1109/ACCESS.2020.3021664>
- Hair Jr., J. F., Page, M., & Brunsveld, N. (2020). *Essentials of Business Research Methods* (Fourth Ed.). Routledge.
- Hamouda, A. E. D. (2014). Using Agile Story Points as an Estimation Technique in CMMI Organizations. *2014 Agile Conference*, 16–23. <https://doi.org/10.1109/AGILE.2014.11>
- Jørgensen, M. (2016). Unit effects in software project effort estimation: Work-hours gives lower effort estimates than workdays. *Journal of Systems and Software*, 117, 274–281. <https://doi.org/10.1016/j.jss.2016.03.048>
- Khatri, S. K., Malhotra, S., & Johri, P. (2016). Use case point estimation technique in software development. In P. Shukla, B and Khatri, SK and Kapur (Ed.), *2016 5th International Conference on Reliability, Infocom Technologies and Optimization (Trends and Future Directions) (ICRITO)* (pp. 123–128). IEEE. <https://doi.org/10.1109/ICRITO.2016.7784938>
- Lenarduzzi, V., Lunesu, I., Matta, M., & Taibi, D. (2015). Functional Size Measures and Effort Estimation in Agile Development: A Replicated Study. In *International Conference on Agile Software Development* (pp. 105–116). Springer. https://doi.org/10.1007/978-3-319-18612-2_9

- López-Martínez, J., Ramírez-Noriega, A., Juárez-Ramírez, R., Licea, G., & Martínez-Ramírez, Y. (2017). Analysis of Planning Poker Factors between University and Enterprise. *2017 5th International Conference in Software Engineering Research and Innovation (CONISOFT)*, 54–60. <https://doi.org/10.1109/CONISOFT.2017.00014>
- López-Martínez, J., Ramírez-Noriega, A., Juárez-Ramírez, R., Licea, G., & Jiménez, S. (2018). User stories complexity estimation using Bayesian networks for inexperienced developers. *Cluster Computing*, *21*(1), 715–728. <https://doi.org/10.1007/s10586-017-0996-z>
- Mahnič, V., & Hovelja, T. (2012). On using planning poker for estimating user stories. *Journal of Systems and Software*, *85*(9), 2086–2095. <https://doi.org/10.1016/j.jss.2012.04.005>
- Malgonde, O., & Chari, K. (2018). An ensemble-based model for predicting agile software development effort. *Empirical Software Engineering*, 1–39. <https://doi.org/10.1007/s10664-018-9647-0>
- Munialo, S. W., & Muketha, G. M. (2016). A Review of Agile Software Effort Estimation Methods. *International Journal of Computer Applications Technology and Research*, *5*(9), 612–618.
- Pasuksmit, J., Thongtanunam, P., & Karunasekera, S. (2021). Towards Just-Enough Documentation for Agile Effort Estimation: What Information Should Be Documented? *2021 IEEE International Conference on Software Maintenance and Evolution (ICSME)*, 114–125. <https://doi.org/10.1109/ICSME52107.2021.00017>
- Popli, R., & Chauhan, N. (2013). A sprint-point based estimation technique in Scrum. *2013 International Conference on Information Systems and Computer Networks*, 98–103. <https://doi.org/10.1109/ICISCON.2013.6524182>
- Popli, R., & Chauhan, N. (2014). Agile estimation using people and project related factors. *2014 International Conference on Computing for Sustainable Global Development (INDIACom)*, 564–569. <https://doi.org/10.1109/IndiaCom.2014.6828023>
- Prakash, B., & Viswanathan, V. (2017). A Survey on Software Estimation Techniques in Traditional and Agile Development Models. *Indonesian*

Journal of Electrical Engineering and Computer Science, 7(3), 867–876.
<https://doi.org/10.11591/ijeecs.v7.i3.pp867-876>

Project-Management.com. (2019). *10 Key Principles of Agile Software Development*. Project Management.Com. <https://project-management.com/10-key-principles-of-agile-software-development/>

Project Management Institute. (2017). *A Guide to the Project Management Body of Knowledge (PMBOK® Guide)* (Sixth Edit). Project Management Institute, Inc.

Ramessur, M. A., & Nagowah, S. D. (2020). Factors Affecting Sprint Effort Estimation. In *Advances in Intelligent Systems and Computing* (Vol. 1089, pp. 507–518). Springer. https://doi.org/10.1007/978-981-15-1483-8_43

Rosa, W., Clark, B. K., Madachy, R., & Boehm, B. (2021). Empirical Effort and Schedule Estimation Models for Agile Processes in the US DoD. *IEEE Transactions on Software Engineering*, 1–1. <https://doi.org/10.1109/TSE.2021.3080666>

Sommerville, I. (2011). *Software Engineering* (9th ed.). Addison-Wesley.

Sudarmaningtyas, P., & Mohamed, R. (2021). A Review Article on Software Effort Estimation in Agile Methodology. *Pertanika Journal of Science and Technology*, 29(2), 837–861. <https://doi.org/10.47836/pjst.29.2.08>

Sudarmaningtyas, P., & Mohamed, R. B. (2020). Extended Planning Poker: A Proposed Model. *2020 7th International Conference on Information Technology, Computer, and Electrical Engineering (ICITACEE)*, 179–184. <https://doi.org/10.1109/ICITACEE50144.2020.9239165>

Trendowicz, A., & Jeffery, R. (2014). *Software Project Effort Estimation: Foundation and Best Practice Guidelines for Success*. Springer International Publishing. <https://doi.org/10.1007/978-3-319-03629-8>

Yuliansyah, H., Qudsiah, S. N., Zahrotun, L., & Arfiani, I. (2018). Implementation of use case point as software effort estimation in Scrum Framework. *IOP Conference Series: Materials Science and Engineering*, 403(1). <https://doi.org/10.1088/1757-899X/403/1/012085>

Zhang, X., Hu, T., Dai, H., & Li, X. (2010). Software development methodologies, trends, and implications. *Information Technology Journal*,

9(8), 173–178.

Appendix I. Questionnaire

EFFORT ESTIMATION QUESTIONNAIRE

Effort estimation is a crucial part of the software development process because effort estimation accuracy can help determine the software delivery time to customers. Besides that, the estimation effort can be used to calculate the cost of developing software. Trendowich (2014) defines effort as a combination of person and time, representing the amount of fully productive work time one person would need to complete a certain work. This questionnaire aims to determine the developer's point of view about the factors contributing to making an effort estimation and the attributes that influence effort estimation accuracy.

This questionnaire consists of three (3) parts. The first part contains questions about personal data. The second part contains factors that influence the estimation value, and the third part contains parameters that make the estimates more accurate. To achieve these objectives, please fill out this questionnaire based on your experiences. Researchers would like to thank you for your participation.

* Required.

1. Email *

PART 1. PERSONAL DATA

Your personal data is protected, not published, and used only in this research.

2. Name *

3. Gender *

Mark only one oval.

Male

Female

9. *Directly or indirectly, I consider the following attributes to create an effort estimation. **

Mark only one oval per row.

	Never (0%)	Occasionally (30%)	Sometimes (50%)	Normally (80%)	Always (100%)
<i>The complexity of software user-interface</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
<i>The complexity of interfaces between software and hardware</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
<i>Variety of technologies that use</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
<i>The use of sophisticated/ novelty technologies</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
<i>Functional requirements complexity</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
<i>Non-functional requirements complexity</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
<i>The difficulty level of coding</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
<i>Database size</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
<i>Database complexity</i>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>

10. *Write three (3) attributes that you normally or always use in effort estimation but not yet mentioned in the previous point.*

11. I generally expressed the value of effort estimation in the form of ... *

Mark only one oval.

- Story points that stated the effort thru the Fibonacci numbers series (1, 2, 3, 5, 8, ...).
- T-shirt sizing, the effort size stated small, medium, or large labels that indicate level complexity.
- Time buckets, the effort estimation expressed in days and hours.

PART 3.
ACCURACY
ATTRIBUTES

Several factors can influence the accuracy of a person in estimates. This section used to know factors affecting someone in making accurate estimates.

12. In my experience, the following attributes can affect a person to produce more accurate estimates. *

Mark only one oval per row.

	No Impact	Low Impact	Fair Impact	High Impact	Very High Impact
Application experience and familiarity.	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
The technical ability of the developer.	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
Effort estimation experience.	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
Involving in many projects.	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
Adequate job experience.	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>
A good track record on previous projects.	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>	<input type="radio"/>

13. Write three (3) attributes that influence a person to produce a more accurate estimation but not yet mentioned in the previous point.

Appendix 2. Survey result

ID RESPO NDEN	Personal Data		Requirements		Design Implementasi						Experience		Domain Knowledge		Technical Ability		Effort																		
	Gender	Job Experience (years)	Project Experience (projects)		Functional requirements complexity		Non-functional requirements		User interface Complexity		Software and hardware interfaces		Diversity of technology		The sophisticated or novelty		Coding Complexity		Database Size		Database Complexity		Job experience	Effort estimation experience		Similar project	Good track record	Technical ability		Involve in many projects		Guess/intuition	Experience	Track record	Attributes
			1	2	1	2	1	2	1	2	1	2	1	2	1	2	1	2	1	2	1	2		1	2			1	2	1	2				
R_01	F	4	2	4	3	3	2	2	3	5	3	2	4	2	4	4	4	4	4	4	3	3	1	0	0	0									
R_02	M	1	2	3	3	4	2	3	3	2	1	1	4	4	5	3	5	4	0	1	1	1													
R_03	F	4	4	5	3	5	5	3	4	5	4	4	5	5	5	5	5	5	0	1	1	1													
R_04	M	2	4	5	4	5	5	5	5	5	3	4	5	5	5	5	5	5	0	1	1	1													
R_05	M	1	4	4	3	4	3	4	4	4	3	4	4	3	4	3	4	4	0	1	0	1													
R_06	M	1	2	4	2	5	2	3	4	5	1	1	3	5	4	4	5	4	0	1	1	1													
R_07	M	4	4	5	4	5	5	5	5	3	1	5	5	5	5	3	5	5	0	1	1	1													
R_08	M	4	4	3	2	2	3	3	3	3	2	3	3	3	3	3	3	3	0	1	1	1													
R_09	F	3	1	3	3	5	5	5	4	3	4	4	5	4	5	5	5	5	0	1	1	1													
R_10	F	2	2	5	4	5	5	5	5	4	4	5	5	5	5	5	5	4	0	1	1	1													
R_11	M	3	4	5	5	5	4	4	4	5	3	4	3	5	5	3	5	3	0	1	1	1													
R_12	M	2	4	4	2	3	4	4	3	5	2	4	3	5	4	3	4	2	1	1	0	1													
R_13	M	1	2	4	3	4	4	4	3	3	3	3	5	5	5	5	5	5	0	0	0	1													
R_14	M	2	3	5	4	5	5	5	5	4	3	3	4	4	4	4	5	4	0	1	1	1													
R_15	F	2	4	4	4	4	3	4	3	5	4	4	5	4	4	5	5	4	0	1	1	1													
R_16	M	2	4	5	3	5	5	3	3	3	3	3	4	4	4	4	5	3	0	1	1	0													
R_17	M	1	1	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	0	1	1	1													
R_18	F	4	4	5	5	5	5	4	4	4	3	4	4	5	5	4	5	4	0	1	0	1													
R_19	M	1	3	4	4	4	4	3	5	3	3	4	4	4	3	4	4	3	0	1	1	1													
R_20	M	2	4	5	4	5	3	4	4	5	4	4	5	5	5	4	4	5	0	1	1	1													
R_21	M	2	3	4	3	4	2	3	3	4	2	3	4	3	5	4	5	5	0	1	1	1													
R_22	M	3	4	5	4	4	2	5	4	5	5	5	5	5	5	5	5	5	0	1	1	1													
R_23	M	1	3	5	4	5	4	4	3	5	3	3	4	3	5	4	5	3	1	0	0	0													
R_24	M	1	2	4	4	4	1	4	4	5	3	4	4	4	4	4	4	5	0	1	1	1													
R_25	M	4	4	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	0	1	1	0													

ID RESPONDEN	Personal Data		Requirements		Design Implementasi						Experience		Domain Knowledge		Technical Ability		Effort					
	Gender	Job Experience (years)	Project Experience (projects)	Functional requirements complexity	Non-functional requirements	User interface Complexity	Software and hardware interfaces	Diversity of technology	The sophisticated or novelty	Coding Complexity	Database Size	Database Complexity	Job experience	Effort estimation experience	Similar project	Good track record	Technical ability	Involve in many projects	Guess/intuition	Experience	Track record	Attributes
				X1	X2	X3	X4	X5	X6	X7	X8	X9	Y1	Y2	Y3	Y4	Y5	Y6	Z1	Z2	Z3	Z4
R_26	M	4	4	5	5	4	4	4	4	4	3	3	5	5	5	5	5	5	0	1	1	0
R_27	M	4	4	5	5	2	3	4	4	3	3	3	3	4	5	4	5	4	0	0	0	1
R_28	M	3	4	5	5	5	5	5	4	5	5	5	5	5	5	4	5	5	1	1	0	1
R_29	M	3	4	5	4	5	3	5	5	5	4	4	4	3	4	3	5	3	0	1	1	0
R_30	M	3	4	5	3	5	2	4	4	5	5	5	4	4	5	4	4	4	0	0	1	0
R_31	M	1	3	4	4	4	4	4	4	4	4	4	3	4	4	4	4	3	0	1	0	0
R_32	M	1	1	5	5	5	5	5	5	5	5	5	2	2	2	2	2	2	0	1	0	0
R_33	M	2	2	4	3	3	3	4	4	5	4	4	4	4	4	4	4	4	0	0	1	0
R_34	M	3	4	4	3	4	4	5	5	5	4	4	5	5	5	4	5	5	1	1	1	0
R_35	M	1	3	3	3	4	3	5	4	5	5	5	5	5	4	4	5	4	1	0	0	0
R_36	M	2	2	5	3	3	3	5	5	5	3	5	4	4	4	5	5	4	0	0	0	1
R_37	F	2	2	5	3	5	4	5	5	3	1	3	2	3	4	2	3	2	0	0	0	1
R_38	F	2	4	5	2	4	1	4	5	4	2	1	2	3	5	5	5	3	0	0	1	0
R_39	M	2	2	4	3	4	4	5	4	4	3	5	3	3	5	3	4	4	0	0	0	1
R_40	M	2	3	5	4	5	5	4	4	3	3	3	3	5	5	3	5	4	1	1	1	1
R_41	M	1	1	5	4	5	4	4	5	5	4	4	4	4	4	4	4	3	1	0	0	0

Significant Factors in Agile Effort Estimation

ORIGINALITY REPORT

9%

SIMILARITY INDEX

6%

INTERNET SOURCES

4%

PUBLICATIONS

2%

STUDENT PAPERS

PRIMARY SOURCES

1

www.pertanika.upm.edu.my

Internet Source

2%

2

Pantjawati Sudarmaningtyas, Rozlina Binti Mohamed. "Extended Planning Poker: A Proposed Model", 2020 7th International Conference on Information Technology, Computer, and Electrical Engineering (ICITACEE), 2020

Publication

1%

3

link.springer.com

Internet Source

1%

4

studentsrepo.um.edu.my

Internet Source

<1%

5

B. Prakash, V. Viswanathan. "A Survey on Software Estimation Techniques in Traditional and Agile Development Models", Indonesian Journal of Electrical Engineering and Computer Science, 2017

Publication

<1%

6

www.jssm.org

Internet Source

<1%

7	Submitted to Regis University Student Paper	<1 %
8	Submitted to The University of Buckingham Student Paper	<1 %
9	nordopen.nord.no Internet Source	<1 %
10	riunet.upv.es Internet Source	<1 %
11	Melvina Autar Ramessur, Soulakshmee Devi Nagowah. "Chapter 43 Factors Affecting Sprint Effort Estimation", Springer Science and Business Media LLC, 2020 Publication	<1 %
12	fishandgame.org.nz Internet Source	<1 %
13	Submitted to University of Northumbria at Newcastle Student Paper	<1 %
14	www.tandfonline.com Internet Source	<1 %
15	Melvina Autar Ramessur, Soulakshmee Devi Nagowah. "A predictive model to estimate effort in a sprint using machine learning techniques", International Journal of Information Technology, 2021 Publication	<1 %

16 Submitted to Laureate Higher Education Group <1 %
Student Paper

17 Yul Derek Davids, Adrian Hadland. "Satisfaction with the Way Democracy is Working in Post-Apartheid South Africa", Politikon, 2008 <1 %
Publication

18 ijcsmc.com <1 %
Internet Source

19 myassignmenthelp.com <1 %
Internet Source

20 www.hbs.edu <1 %
Internet Source

21 Asnawi, Ani Liza, Gravell, Andrew, Wills, Gary. "Factor Analysis: Investigating Important Aspects for Agile Adoption in Malaysia" <1 %
Internet Source

22 Mohammad Azzeah, Ali Bou Nassif, Imtinan Basem Attili. "Predicting software effort from use case points: A systematic review", Science of Computer Programming, 2021 <1 %
Publication

23 doc-pak.undip.ac.id <1 %
Internet Source

24 ebin.pub

Internet Source

<1 %

25

ndl.ethernet.edu.et

Internet Source

<1 %

26

www.abacademies.org

Internet Source

<1 %

27

R. C. Sandeep, Mary Sánchez-Gordón, Ricardo Colomo-Palacios, Monica Kristiansen.

"Chapter 8 Effort Estimation in Agile Software Development: A Exploratory Study of Practitioners' Perspective", Springer Science and Business Media LLC, 2022

Publication

<1 %

28

digitalcommons.odu.edu

Internet Source

<1 %

29

eprints.uad.ac.id

Internet Source

<1 %

30

etd.uum.edu.my

Internet Source

<1 %

31

sol.sbc.org.br

Internet Source

<1 %

32

www.frontiersin.org

Internet Source

<1 %

33

Anupama Kaushik, Devendra Kumar Tayal, Kalpana Yadav. "chapter 47 The Role of

<1 %

Neural Networks and Metaheuristics in Agile Software Development Effort Estimation", IGI Global, 2022

Publication

34

Marta Fernandez-Diego, Erwin R. Mendez, Fernando Gonzalez-Ladron-De-Guevara, Silvia Abrahao, Emilio Insfran. "An Update on Effort Estimation in Agile Software Development: A Systematic Literature Review", IEEE Access, 2020

Publication

<1 %

35

jurnal.ugm.ac.id

Internet Source

<1 %

Exclude quotes On

Exclude matches Off

Exclude bibliography On
